

ID	Task Name	Duration	Start	Finish	% Complete												
						Nov	2026 Jan	Mar	May	Jul	Sep	Nov	2027 Jan	Mar	May	Jul	
1	Design Deliverables	55 days	Tue 2/24/26	Mon 5/11/26	0%												
2	Draft Closure Report, Drawings, and Specs	30 days	Tue 2/24/26	Mon 4/6/26	0%												
3	Submit Draft Closure Report, Drawings, and Specs	0 days	Mon 4/6/26	Mon 4/6/26	0%												
4	Client Review	10 days	Tue 4/7/26	Mon 4/20/26	0%												
5	Resolve Client Comments	10 days	Tue 4/21/26	Mon 5/4/26	0%												
6	Client Backcheck RTCs	5 days	Tue 5/5/26	Mon 5/11/26	0%												
7	Final Closure Report, Drawings, and Specs	0 days	Mon 5/11/26	Mon 5/11/26	0%												
8	Construction Phase 1	50 days	Tue 4/21/26	Mon 6/29/26	0%												
9	Submit Product Data	19 days	Tue 4/21/26	Fri 5/15/26	0%												
10	Mobilization / Site Preparation	4 days	Mon 5/18/26	Thu 5/21/26	0%												
11	Haul Cover Material from Borrow Site to Laydown Area	8 days	Fri 5/22/26	Tue 6/2/26	0%												
12	Construct Access Roads / Site Clearing	2 days	Fri 5/22/26	Mon 5/25/26	0%												
13	Site Cleaning and Loading of Historical Equipment	3 days	Fri 5/22/26	Tue 5/26/26	0%												
14	Delivery of Historical Equipment to Museum	0 days	Tue 5/26/26	Tue 5/26/26	0%												
15	Placement of Waste Rock into Decline	2 days	Tue 5/26/26	Wed 5/27/26	0%												
16	Construction of Bulkhead	4 days	Thu 5/28/26	Tue 6/2/26	0%												
17	Placement of Waste Rock into Portal	4 days	Thu 5/28/26	Tue 6/2/26	0%												
18	Placement and Grading of Remaining Waste Rock	5 days	Wed 6/3/26	Tue 6/9/26	0%												
19	Hauling of Cover Material from Laydown Area to Site	8 days	Tue 5/26/26	Thu 6/4/26	0%												
20	Construction of Cover	5 days	Wed 6/10/26	Tue 6/16/26	0%												
21	Seeding and Site Restoration	3 days	Wed 6/17/26	Fri 6/19/26	0%												
22	Partial Demobilization and Contingency	6 days	Mon 6/22/26	Mon 6/29/26	0%												
23	Construction Hiatus	23 days	Tue 6/30/26	Thu 7/30/26	0%												
24	Construction Phase 2	18 days	Mon 8/3/26	Wed 8/26/26	0%												
25	Labor Mobilization	2 days	Mon 8/3/26	Tue 8/4/26	0%												
26	Installation of Fencing and Signage	5 days	Wed 8/5/26	Tue 8/11/26	0%												
27	Confirmation Sampling and Analysis	5 days	Wed 8/5/26	Tue 8/11/26	0%												
28	Removal and Restoration of Access Roads and Stockpiling Area	8 days	Wed 8/12/26	Fri 8/21/26	0%												
29	Demobilization	3 days	Mon 8/24/26	Wed 8/26/26	0%												
30	Record Documents	200 days	Wed 8/12/26	Tue 5/18/27	0%												
31	Lab Data Reports	30 days	Wed 8/12/26	Tue 9/22/26	0%												
32	As-built Drawings	15 days	Thu 8/27/26	Wed 9/16/26	0%												
33	Subcontractor Project Reports	35 days	Wed 9/23/26	Tue 11/10/26	0%												
34	Draft Project Reports from Subs	20 days	Wed 9/23/26	Tue 10/20/26	0%												
35	Review of Project Reports from Subs	10 days	Wed 10/21/26	Tue 11/3/26	0%												
36	Final Project Reports from Subs	5 days	Wed 11/4/26	Tue 11/10/26	0%												
37	LTM Report	80 days	Wed 9/23/26	Tue 1/12/27	0%												
38	Draft LTM Report	30 days	Wed 9/23/26	Tue 11/3/26	0%												

Project: Schmitt Decline Mine
Date: Thu 4/23/26

Task

Split

Milestone

Summary

◆

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

◆

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Manual Task

Finish-only

External Tasks

External Milestone

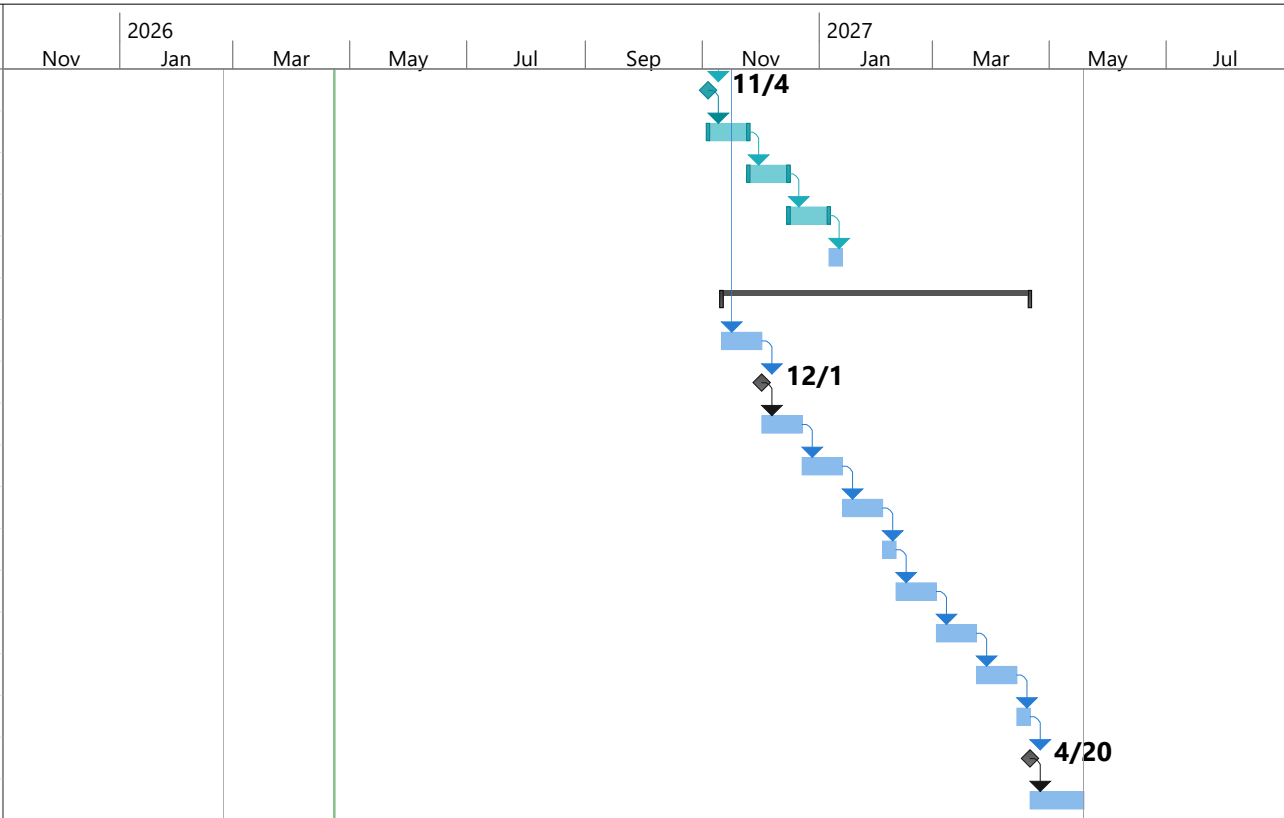
Start-only

Progress

Manual Progress

Deadline

Page 1

ID	Task Name	Duration	Start	Finish	% Complete														
						Nov	2026 Jan	Mar	May	Jul	Sep	Nov	2027 Jan	Mar	May	Jul			
39	Submit Draft LTM Report	0 days	Wed 11/4/26	Wed 11/4/26	0%														
40	NMED-EMNRD Review	15 days	Wed 11/4/26	Tue 11/24/26	0%														
41	Resolve Comments/ Submit Draft-Final LTM Report	15 days	Wed 11/25/26	Tue 12/15/26	0%														
42	NMED-EMNRD Backcheck	15 days	Wed 12/16/26	Tue 1/5/27	0%														
43	Submit Final LTM Report	5 days	Wed 1/6/27	Tue 1/12/27	0%														
44	Finalize Closure Report	115 days	Wed 11/11/26	Tue 4/20/27	0%														
45	Update Closure Report with Construction Documentation	15 days	Wed 11/11/26	Tue 12/1/26	0%														
46	Submit Draft to NMED-EMNRD	0 days	Tue 12/1/26	Tue 12/1/26	0%														
47	NMED-EMNRD Review	15 days	Wed 12/2/26	Tue 12/22/26	0%														
48	Resolve Comments	15 days	Wed 12/23/26	Tue 1/12/27	0%														
49	NMED-EMNRD Backcheck	15 days	Wed 1/13/27	Tue 2/2/27	0%														
50	Submit Draft-Final to SLO	5 days	Wed 2/3/27	Tue 2/9/27	0%														
51	SLO Review	15 days	Wed 2/10/27	Tue 3/2/27	0%														
52	Resolve Comments	15 days	Wed 3/3/27	Tue 3/23/27	0%														
53	SLO and NMED-EMNRD Backcheck	15 days	Wed 3/24/27	Tue 4/13/27	0%														
54	Finalize Report	5 days	Wed 4/14/27	Tue 4/20/27	0%														
55	Submit Final Closure Report	0 days	Tue 4/20/27	Tue 4/20/27	0%														
56	Final Payment Applications	20 days	Wed 4/21/27	Tue 5/18/27	0%														

Project: Schmitt Decline Mine
Date: Thu 4/23/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress
