



April 19, 2022

RECEIVED
By PSTB at 1:46 pm, Apr 19, 2022

Ms. Renee Romero
New Mexico Environment Department
Petroleum Storage Tank Bureau
1914 West Second Street
Roswell, New Mexico 88201-1712

Re: Fence Installation Letter Report
Former Y Station, 721 Commerce Way, Clovis, New Mexico
Facility #53742, Release ID #4746, WPID #4224

Dear Ms. Romero:

Daniel B. Stephens & Associates, Inc. (DBS&A) is pleased to submit this letter report documenting the equipment compound fence installation at the Former Y Station State Lead Site in Clovis, NM. EnviroWorks, LLC (EnviroWorks), of Edgewood, New Mexico, served as the general contractor for the work. This report summarizes the work that was performed to install the security fence around the new equipment compound. The invoice for the work is provided in Attachment 1. Photographs of the new fence are provided in Attachment 2.

On April 11-14, 2022, American Fence installed the 8-foot-tall chain link fence around the equipment compound. Holes were drilled using a skid steer auger attachment, and new fence posts were cemented in concrete that was hand mixed on-site. The chain link fence was completed with tan privacy slats and three strands of barbed wire around the top of the fence for added security. Two 12-foot wide double swing gates were also installed per the engineering drawings. Both gates are locked with heavy-duty combination locks.

DBS&A intends to invoice the full approved amount for Deliverable ID #4224-5. If you have any questions or require additional information, please contact us at (505) 822-9400.

Sincerely,

DANIEL B. STEPHENS & ASSOCIATES, INC.

Thomas Golden, P.E.
Senior Engineer

Grace Herrmann, E.I.
Staff Engineer

Attachment

cc: Katherine MacNeil, NMED PSTB

Daniel B. Stephens & Associates, Inc.

6020 Academy NE, Suite 100 505-822-9400

Attachment 1
Manufacturer Invoice

EnviroWorks, LLC
 Edgewood, NM 87015

Invoice

Date	Invoice #
4/14/2022	21262

Bill To
Daniel B. Stephens & Associates, Inc Daniel B. Stephens & Associates, Inc. 6020 Academy Road NE, Suite 100 Albuquerque, NM 87109

Ship To

P.O. Number	Terms	Rep	Ship	Via	F.O.B.	Project
	Net 30		4/14/2022			21-65 Y Station

Quantity	Item Code	Description	U/M	Price Each	Amount
1	Revenue-Constru...	WO # db18.1157.00.REM00.0006 Fencing Attn: Tom Golden		21,250.00	21,250.00

565 **ACCOUNTING INFORMATION**

PROJECT #/PHASE/TASK	AMOUNT
DB18.1157.00.REM00.0005	\$21,250.00

 4/15/22

Approval **Date**

Total				\$21,250.00
--------------	--	--	--	-------------

Attachment 2

**Photographic
Documentation**



1. American Fence installed the new 8-foot tall chain link fence the week of April 11, 2022.




2. Privacy slats were installed on all chain link fence panels. Three strands of barbed wire were installed along the top of the fence.





3. A 12-foot wide double swing gate was installed on the southeast corner of the fence near the groundwater treatment container doors.

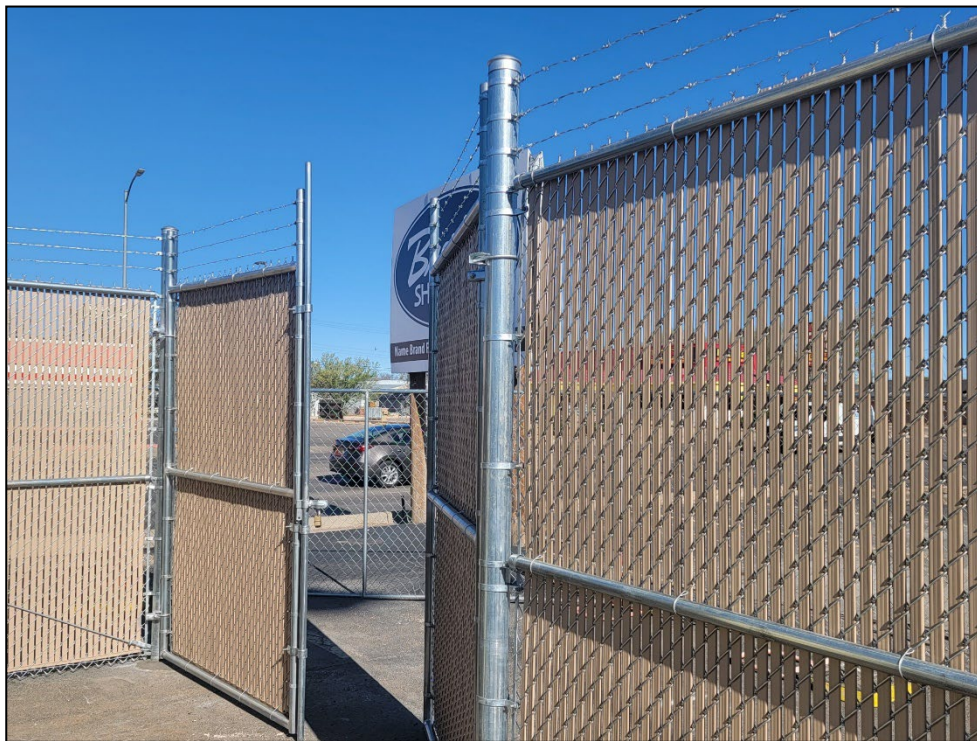

4. A 12-foot wide double swing gate was also installed on the northwest corner of the fence near the SVE container doors. Both gates are secured with a heavy-duty combination lock.

